Project Plan

< Hairstylist Booking Application >

Industry Partner	Erick Henrique Lima Fernandes
Primary Instructor	Anjana Shah
Team Member	Lucas Tavares Criscuolo
Team Member	Mateus de Souza Carvalho Melco Sfeir
Team Member	Gustavo Miranda
Team Member	Renan Yoshida Avelan
Team Member	

Document Revision History

Revision #	Date
0.1	2025-09-31
1.0	2025-10-01

Table of Contents

1. Executive Summary

The following describes the project to be executed.

Objective	• Replace manual DM/phone scheduling with a reliable self-service booking platform. • Reduce no-shows and double bookings via automated confirmations/reminders. • Enhance the hairstylist's digital presence with branding, testimonials, and portfolio.
Corporate Goals Addressed	• Digitization of business processes for small businesses. • Improved customer experience and accessibility. • Establishing trust, discoverability, and growth opportunities.
Planned Start Date	September 15, 2025
Planned End Date	March 27, 2026

2. Project Approvers, Reviews and Distribution List

Approvers, reviewers and distribution list

Project Role	Name	E-mail	Date
Capstone Instructor	Anjana Shah	ashah@georgebrown.ca	31-09-2025
Client (Hairstylist)	Erick Henrique Lima Fernandes		31-09-2025
Team Member	Lucas Tavares Criscuolo	lucas.tavarescriscuolo@georgebrown.ca	31-09-2025
Team Member	Gustavo Miranda	gustavo.miranda@georgebrown.ca	31-09-2025
Team Member	Renan Yoshida	renan.yoshidaavelan@georgebrown.ca	31-09-2025

	Avelan		
Team Member	Mateus de Souza Carvalho Melco Sfeir	mateus.desouzacarvalhomelcosfeir@georgebrown.ca	31-09-2025

3. Scope

Define the sum total of all of its products and their requirements or features.

In Scope	Out of Scope
Web and mobile client booking flow (book, reschedule, cancel).	Payment integration.
Admin dashboard: manage services, hours, blackout dates, appointments.	Multi-staff/multi-location features (future).
Email notifications (create, cancel, reschedule).	Advanced analytics.
Portfolio & Testimonials (with admin approval & consent).	Public commenting features.
Blog module (basic SEO support).	
Branding: logo, colors, typography applied consistently.	

4. Deliverables

This project will deliver the following.

Deliverable	Description
Online Booking System	Web & mobile client booking flow with email confirmations.
Admin Dashboard	Hairstylist tool to manage services, availability, bookings, and testimonials.
Branding Package	Logo, palette, typography for consistent presentation.
Portfolio & Testimonials	Gallery and feedback with admin approval/consent logging.

Blog Module (optional)	Content publishing with categories/tags, SEO fields.
Mobile App Prototype	Companion app mirroring client booking & browsing features.

5. Assumptions

This project makes the following assumptions;

- Single stylist, single location, one calendar.
- Notifications delivered via email only.
- Client provides branding inputs, photos, and testimonials.
- Project resources (hosting, DB, email service) available in free/low-cost tiers.

6. Dependencies

The following are the internal and external dependencies that will have to be acknowledged and addressed;

- Reliable hosting and transactional email service.
- Timely feedback and approvals from Erick (client).
- Team availability and workload distribution.
- Adherence to college deadlines and sprint structure.

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
Double-booking due to technical bug	H	M	Test booking flow thoroughly; include calendar sync logic.
Email not delivered (spam/delays)	M	H	Choose reliable provider;

			monitor sender reputation.
Scope creep (extra features requested)	H	M	Freeze scope after approval; track as future enhancements.
Team member unavailability	M	M	Redistribute tasks; document thoroughly for continuity.
Data privacy concerns (photos/testimonials)	M	L	Store explicit consent; allow removal on request.

8. Communication

Reporting

The following reports will be produced;

Report	Audience	Frequency
Weekly Progress Report	Instructor & Team End of Sprint	Weekly
Sprint Deliverables	Instructor	End of Sprint

Meetings

The following meetings/communication will be established;

Meeting	Purpose	Attendees	Frequency
Team Sync	Review progress, assign tasks	All team members	Weekly
Client Meeting	Demo progress, gather feedback	Erick + Team	Weekly
Instructor Check-in	Ensure project alignment	Instructor + Team	Weekly

9. Task Listing (WBS- Work Breakdown Structure)

The following resource proposal template summarizes the resource hours committed to this project, upon final approval of this document.

Reference	Tasks	Duration	Dependency
A	Project Planning (Sprint 2)	2 Weeks	-----
B	Requirements and Analysis	3 Weeks	A
B1	Stakeholder Interviews	1 Week	A
B2	User Stories & Personas Validation	1 Week	A
B3	High-Level Requirements Refinement	1 Week	A
C	Design (UI/UX, Branding)	3 Weeks	B
C1	Wireframes (Booking/Admin views)	1 Week	B
C2	Branding Package (logo, palette, etc.)	1 Week	B
C3	Prototype Review with Client	1 Week	C1, C2
D	Development Phase	8 Weeks	C
D1	Booking Flow (Web)	3 weeks	C
D2	Admin Dashboard (Web)	2 Weeks	D1
D3	Portfolio % Template Module	2 Weeks	D1, D2
D4	Blog Module (Optional)	2 Weeks	D3
D5	Mobile App Prototype	4 Weeks	D1, D2
E	Testing and QA	3 Weeks	D
E1	Unit Testing	1 Week	D
E2	Integration Testing	1 Week	E1
E3	User Acceptance Testing	1 Week	E2
F	Deployment and Final Delivery	2 Weeks	E
F1	Final Deployment Preparation	1 Week	E
F2	Documentation & Handover	1 Week	F1

10. Gantt Chart

Create a detailed Gantt Chart from your Task Listing(Use any software tool and paste the image or upload as a separate file that can be opened as pdf/doc/xls)

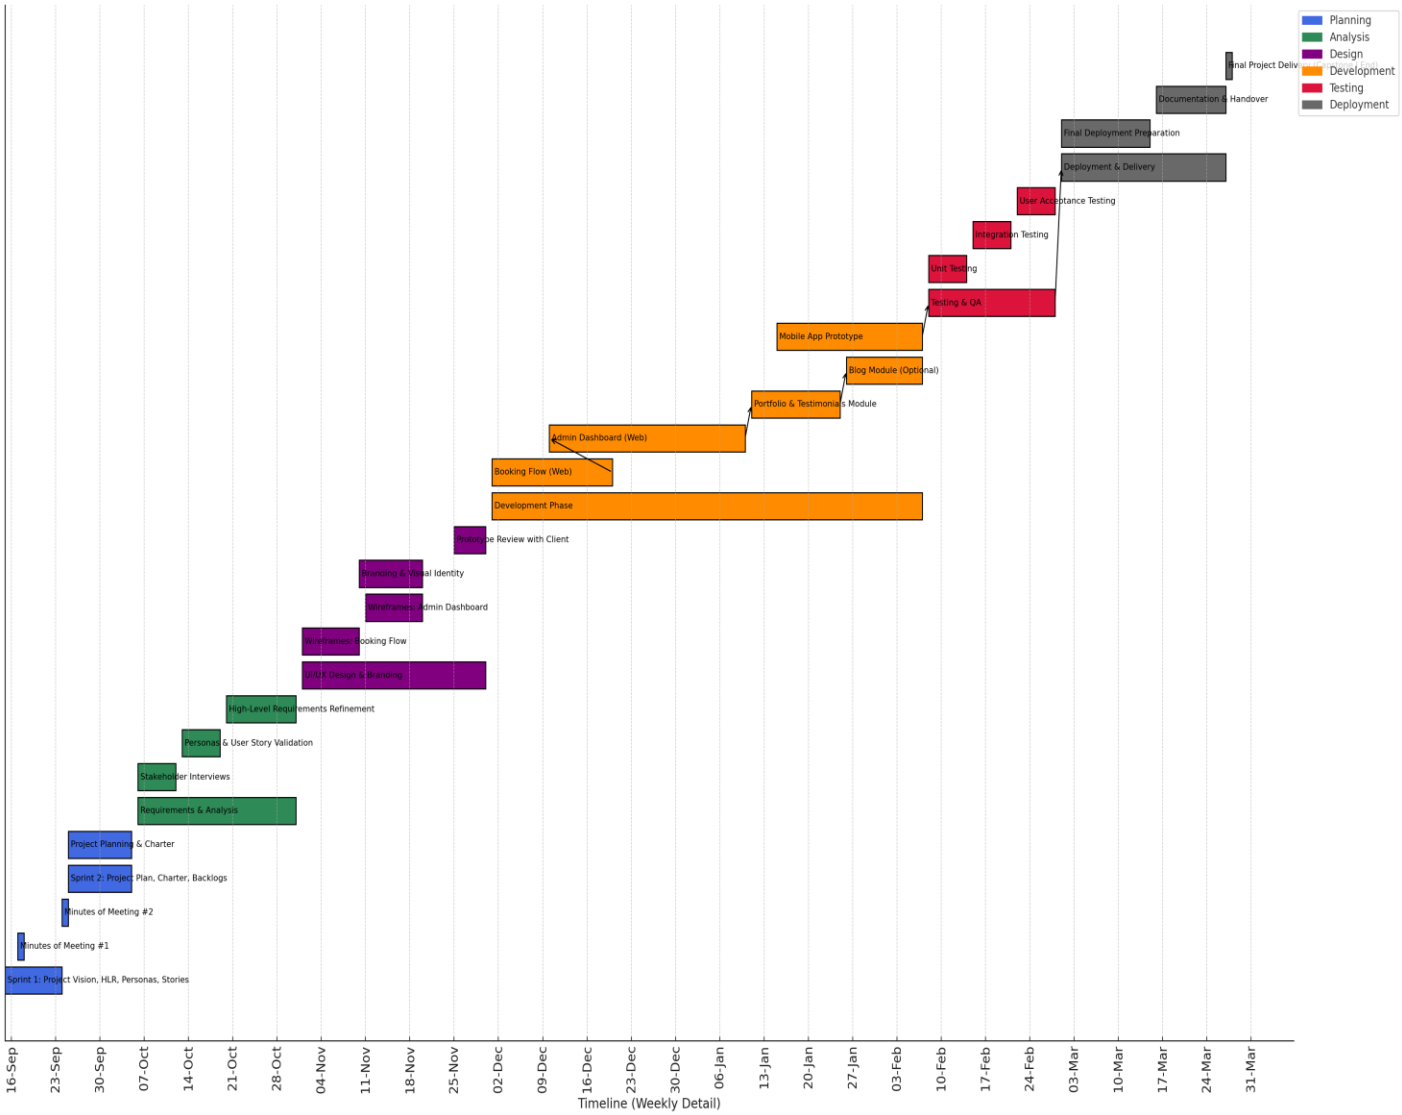

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Sprint 1 Deliverables Approved	Sept 24, 2025	Team + Instructor
Minutes of Meeting #1 Completed	Sept 17, 2025	Team
Minutes od Meeting #2 Completed	Sept 24, 2025	Team
Sprint 2: Project Plan, Team Charter, Backlogs	Oct 5, 2025	Team + Instructor
Project Planning & Charter Approved	Oct 5, 2025	Team + Instructor
Requirements & Analysis Complete	Oct 31, 2025	Team

UI/UX Design & Branding Complete	Nov 30, 2025	Lucas (lead)
Prototype Review with Client	Dec 1, 2025	Erick (Client)
Sprint 3: Requirements, Analysis & Design	Dec 12, 2025	Team + Instructor
Booking Flow MVP Completed	Dec 20, 2025	Gustavo (lead)
Admin Dashboard MVP Completed	Jan 10, 2025	Renan (lead)
Portfolio & Testimonials Module	Jan 25, 2025	Mateus (lead)
Blog Module (Optional)	Feb 7, 2026	Mateus (lead)
Mobile App Prototype Ready	Feb 7, 2026	Gustavo + Mateus
Unit Testing Completed	Feb 14, 2026	Team
User Acceptance Testing Completed	Feb 21, 2026	Team
User Acceptance Testing	Feb 28, 2026	Erick + Team
Sprint 4: Wireframes/Prototype + technical Requisition	Mar 12, 2026	Team + instructor
Final Deployment Preparation	Mar 15, 2026	Team
Documentation & Handover	Mar 27, 2026	Team
Final Project Delivery (Capstone End)	Mar 27, 2026	Team + Instructor

12. RAM – Responsibility Assignment Matrix

Create a RAM from your Task Listing. A sample is shown below:

Project Team Responsibilities

Project Name: New Package Installation
Project Manager: Al Q. Hall

Task	John	Frank	Linda	Jean	Larry
Assess Requirements	P	S	S		
Design Business System			S	P	
Modify Purchased Package	S	P			
Modify In-House Procedures			P	S	
Testing	S				P
Implement New Package		P		S	
Train Staff		S		S	P

P = Primary S = Secondary

Project Name: Hairstylist Booking Web Application
Project Manager: Team BrazWebDes (shared responsibility)

Task / Deliverable	Lucas	Gustavo	Renan	Mateus	Erick (Client)
Project Planning & Charter	**P**	S	S	S	
Requirements & Analysis	S	**P**	S	S	**S**
UI/UX & Branding Design	**P**	S	S	S	**S**
Booking System (Web)	S	**P**	S	S	I
Admin Dashboard (Web)	S	S	**P**	S	I
Portfolio & Testimonials	S	S	S	**P**	I
Blog Module (Optional)	S	S	S	**P**	I
Mobile App Prototype	S	**P**	S	**P**	I
Testing & QA	**P**	**P**	**P**	**P**	C
Documentation & Final Delivery	**P**	S	S	S	I

- **P = Primary** (responsible for leading the task)
- **S = Secondary** (support role)
- **C = Consulted**
- **I = Informed**

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Team Member - Developer	Lucas Tavares Criscuolo	Lucas Tavares Criscuolo	2025-10-01
Team Member - Developer	Gustavo Miranda	Gustavo Miranda	2025-10-01
Team Member - Developer	Renan Yoshida Avelan	Renan Yoshida Avelan	2025-10-01
Team Member - Developer	Mateus De Souza Carvalho Melco Sfeir	Mateus De Souza Carvalho Melco Sfeir	2025-10-01
